




Task Name	Duration	Start	Finish
1	50 days	Wed 4/26/06	Wed 7/5/06
2	5 days	Wed 4/26/06	Tue 5/2/06
8	0 days	Wed 5/3/06	Wed 5/3/06
9	7 days	Wed 4/26/06	Thu 5/4/06
15	37 days	Wed 5/10/06	Thu 6/29/06
16	24 days	Wed 5/10/06	Mon 6/12/06
59	18 days	Thu 6/1/06	Mon 6/26/06
120	3 days	Tue 6/27/06	Thu 6/29/06
126	0.5 days	Fri 6/30/06	Fri 6/30/06
129	0 days	Wed 7/5/06	Wed 7/5/06

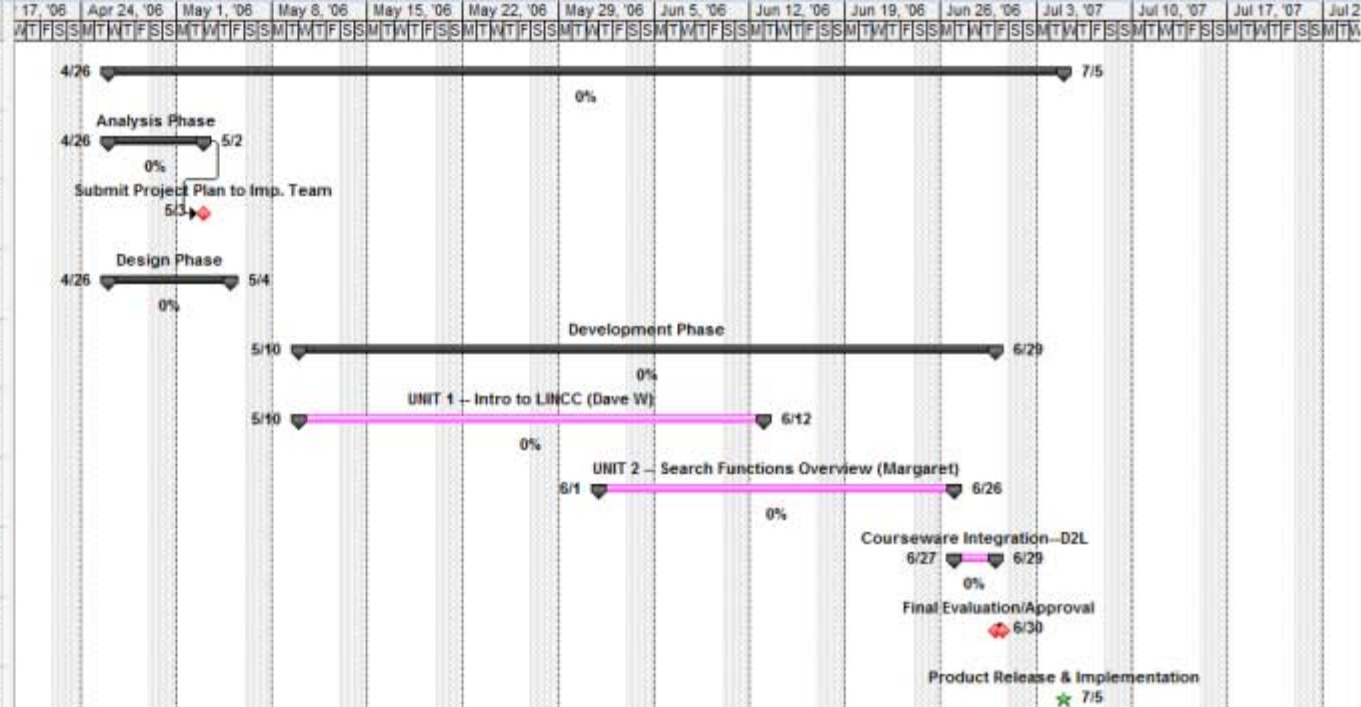

Task Name	Duration	Start	Finish
Development Phase	37 days	Wed 5/10/06	Thu 6/29/06
UNIT 1 – Intro to LINCC (Dave W)	24 days	Wed 5/10/06	Mon 6/12/06
Unit 1: LSC Content Components (Dave W)	15.5 days	Wed 5/10/06	Wed 5/31/06
Unit 1: Coaching_Coordinating_QA_PMP update	13 days	Wed 5/10/06	Fri 5/26/06
Unit 1 - Lesson 1	3 days	Wed 5/10/06	Fri 5/12/06
Unit 1 - Lesson 2	7 days	Mon 5/15/06	Tue 5/23/06
Unit 1 - Lesson 3	5 days	Wed 5/24/06	Tue 5/30/06
Unit 1: Test	0.5 days	Wed 5/31/06	Wed 5/31/06
Unit 1 Review cycle	5 days	Wed 5/31/06	Wed 6/7/06
Unit 1: Wayne Dev.–Processing & Integration	21 days	Mon 5/15/06	Mon 6/12/06
UNIT 2 – Search Functions Overview (Margaret)	18 days	Thu 6/1/06	Mon 6/26/06
Courseware Integration–D2L	3 days	Tue 6/27/06	Thu 6/29/06
Final Evaluation/Approval	0.5 days	Fri 6/30/06	Fri 6/30/06
Product Release & Implementation	0 days	Wed 7/5/06	Wed 7/5/06

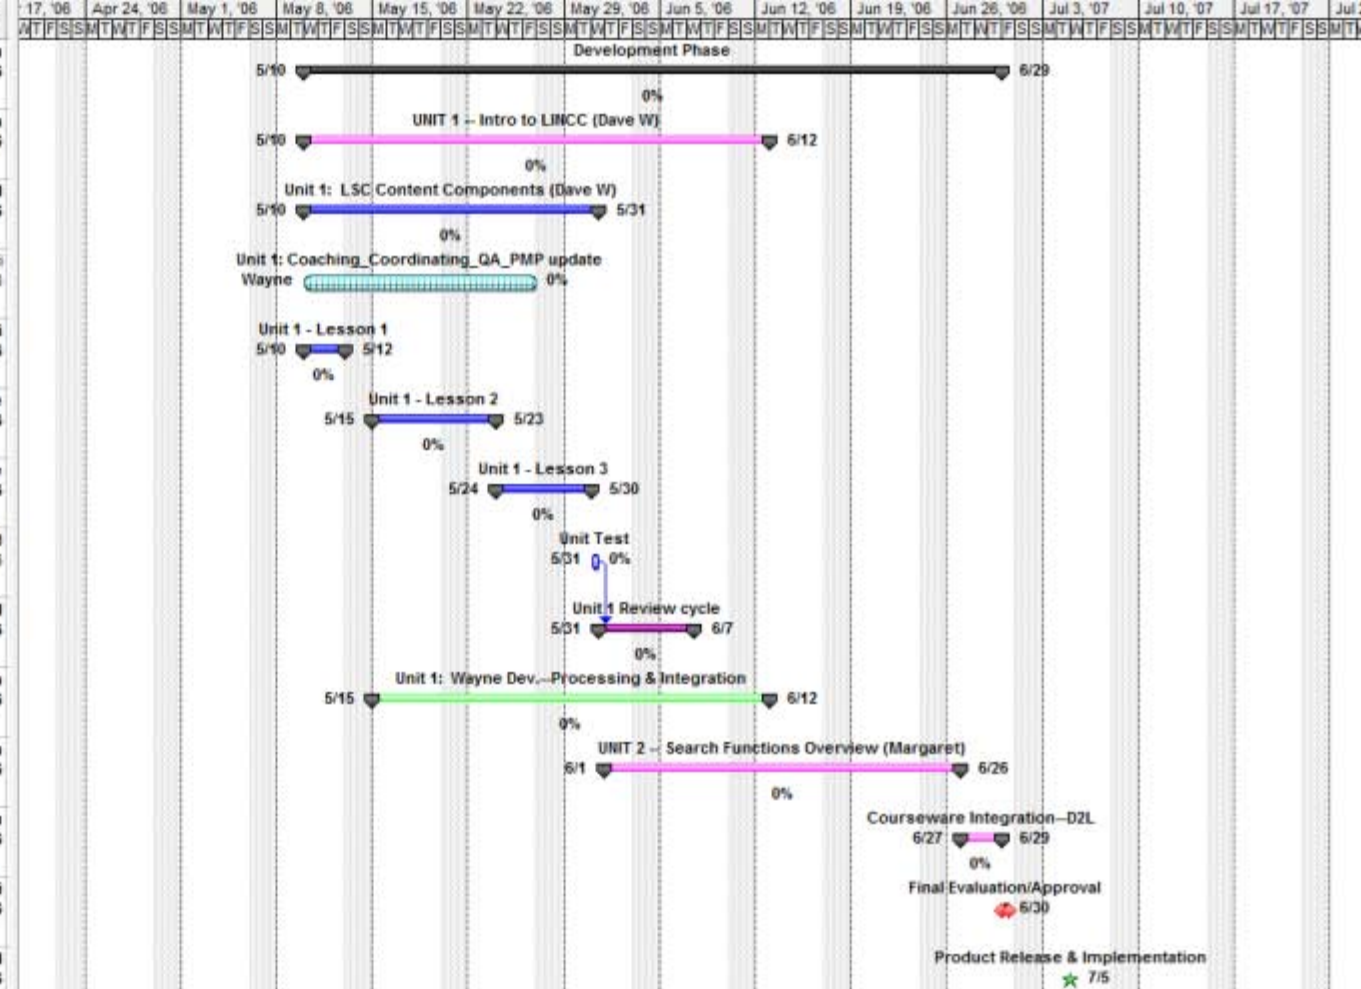

Task Name	Duration	Start	Finish
9 Design Phase	7 days	Wed 4/26/06	Thu 5/4/06
15 Development Phase	37 days	Wed 5/10/06	Thu 6/29/06
16 UNIT 1 -- Intro to LINCC (Dave W)	24 days	Wed 5/10/06	Mon 6/12/06
17 Unit 1: LSC Content Components (Dave W)	15.5 days	Wed 5/10/06	Wed 5/31/06
18 Unit 1: Coaching_Coordinating_QA_PMP update	13 days	Wed 5/10/06	Fri 5/26/06
19 Unit 1 - Lesson 1	3 days	Wed 5/10/06	Fri 5/12/06
20 Unit 1 Lesson 1: Prepare practice script & training database	1 day	Wed 5/10/06	Wed 5/10/06
21 Unit 1 Lesson 1: Demo Animations (ViewletBuilder)	0.5 days	Thu 5/11/06	Thu 5/11/06
22 Unit 1 Lesson 1: Static Screens & graphics	0.5 days	Thu 5/11/06	Thu 5/11/06
23 Unit 1 Lesson 1: Text --Word Files	0.5 days	Fri 5/12/06	Fri 5/12/06
24 Unit 1 Lesson 1: Quiz	0.5 days	Fri 5/12/06	Fri 5/12/06
25 Unit 1 - Lesson 2	7 days	Mon 5/15/06	Tue 5/23/06
31 Unit 1 - Lesson 3	5 days	Wed 5/24/06	Tue 5/30/06
37 Unit 1: Test	0.5 days	Wed 5/31/06	Wed 5/31/06
38 Unit 1 Review cycle	5 days	Wed 5/31/06	Wed 6/7/06

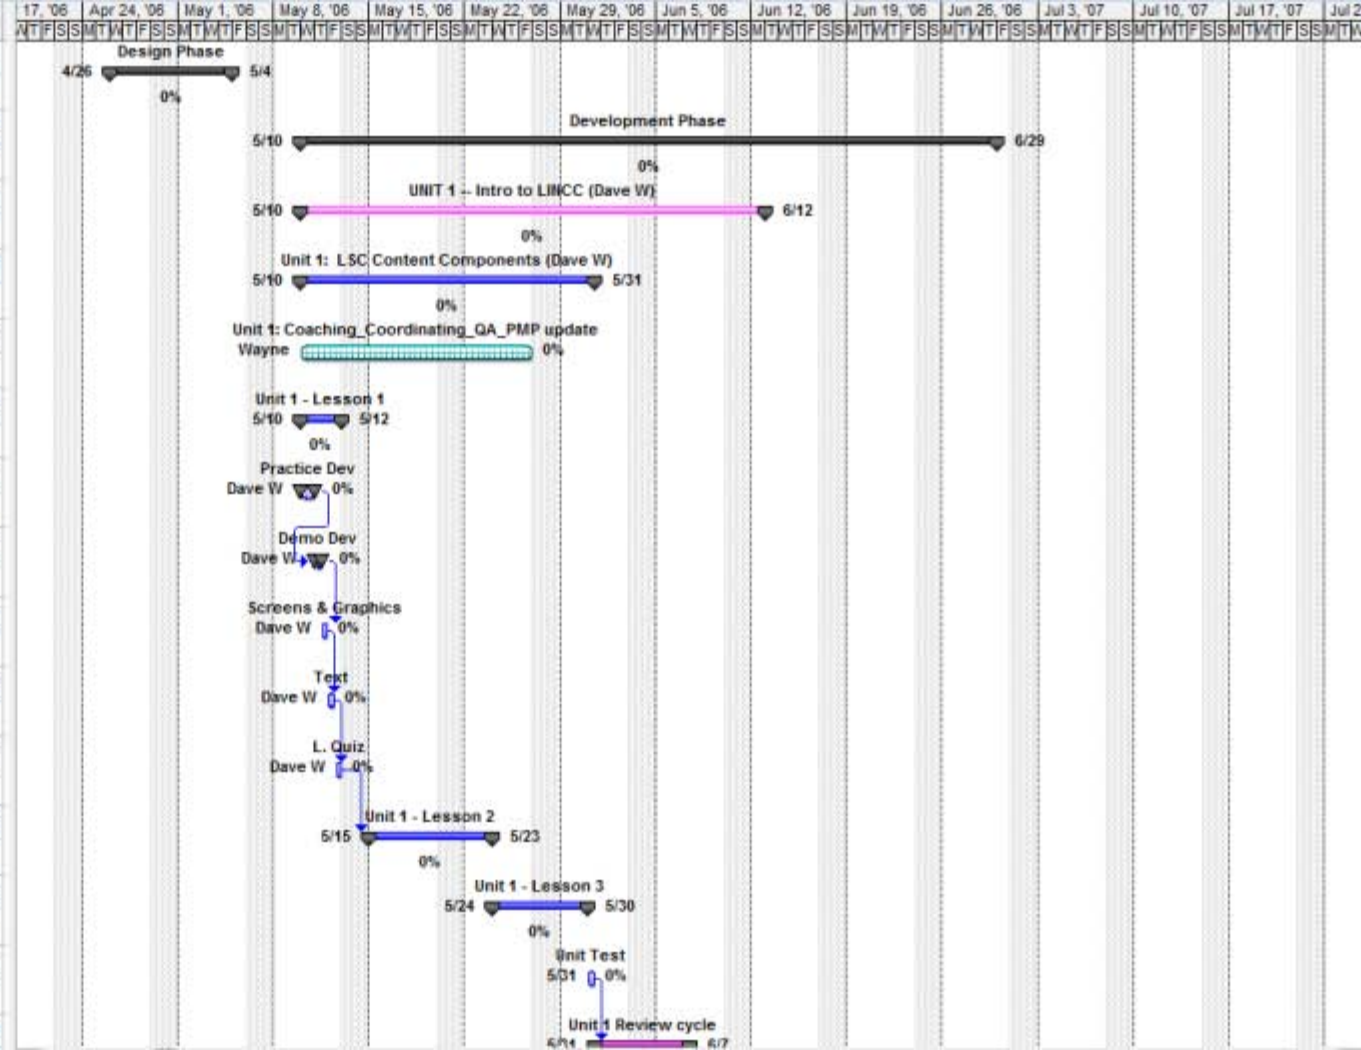

Task Name	Duration	Start	Finish
Unit 1: Test	0.5 days	Wed 5/31/06	Wed 5/31/06
Unit 1 Review cycle	5 days	Wed 5/31/06	Wed 6/7/06
Unit 1 prep for review cycle (ID comments & Master file setup)	0.5 days	Wed 5/31/06	Wed 5/31/06
Unit 1 Review cycle: Wayne comment review	0.5 days	Thu 6/1/06	Thu 6/1/06
Unit 1: all LSCs review complete	1 day	Thu 6/1/06	Fri 6/2/06
Unit 1: LSCs comment changes	0.5 days	Fri 6/2/06	Fri 6/2/06
Unit 1: Editorial Review	2 days	Mon 6/5/06	Tue 6/6/06
Unit 1: SME final changes	0.5 days	Wed 6/7/06	Wed 6/7/06
Unit 1: Wayne Dev.--Processing & Integration	21 days	Mon 5/15/06	Mon 6/12/06
UNIT 2 -- Search Functions Overview (Margaret)	18 days	Thu 6/1/06	Mon 6/26/06
Courseware Integration--D2L	3 days	Tue 6/27/06	Thu 6/29/06
Final Evaluation/Approval	0.5 days	Fri 6/30/06	Fri 6/30/06
Final Review	0.5 days	Fri 6/30/06	Fri 6/30/06
Evaluation Phase completion Review and approval	0 days	Fri 6/30/06	Fri 6/30/06
Product Release & Implementation	0 days	Wed 7/5/06	Wed 7/5/06

